



Magnox

Magnox Ltd is owned by the Nuclear Decommissioning Authority

Dungeness A Site Report to Site Stakeholder Group – November 2022

Chris Milne

Site Integration Manager Dungeness A Site



Safety and compliance



- Unfortunately a hand injury occurred on site. In response:
 - We launched an investigation
 - Held a two-day safety stand-down to talk and listen to our workforce
 - Using feedback from our teams we have developed a list of priority safety targets
- We are committed to a continued focus on safety and improvement
- An Emergency Services Day was recently held where representatives from all services attended site.



Storm damage update

- Work has taken place to make the reactor building safe and secure following the winter storm damage earlier this year



Dungeness Sustainability Group



- DNA is leading a company-wide initiative to install electric vehicle charging stations.
- Low carbon emission technology is being introduced such as Solar Powered Street Lighting and Hybrid Generators.



Business Planning



- We're expecting some funding constraints over the next couple of years and all Magnox Sites are currently preparing Business Plans to address this.
- The Dungeness Business Plan will be presented to the Magnox Exec in December.
- This may involve a slower rate of progress for some projects but we're not expecting a significant impact to our programme of work.



Recap on current key projects – waste projects

- The site has met a milestone to safely transfer circa 5m³ of contaminated sludge
- Non active commissioning of the Wet Waste Transfer facility is in progress
- The concrete pour for the new ILW Processing Facilities is planned for February with up to 8 lorries per day expected over a 2 week period.




Boiler down project – next steps

Filling of tunnels and culverts – enabling works which, once complete, will provide space for contractors to mobilise plant and equipment for demolition and boiler removal

Next activity:

- Culvert infill – up to three lorries per day on weekdays from end of November 2022 to mid January 2023. No lorry movements over the two-week Christmas and New Year period
- Filling of the turbine hall basement – spring 2023 to early 2024
- Steam and cable tunnels infill – work planned for summer 2023

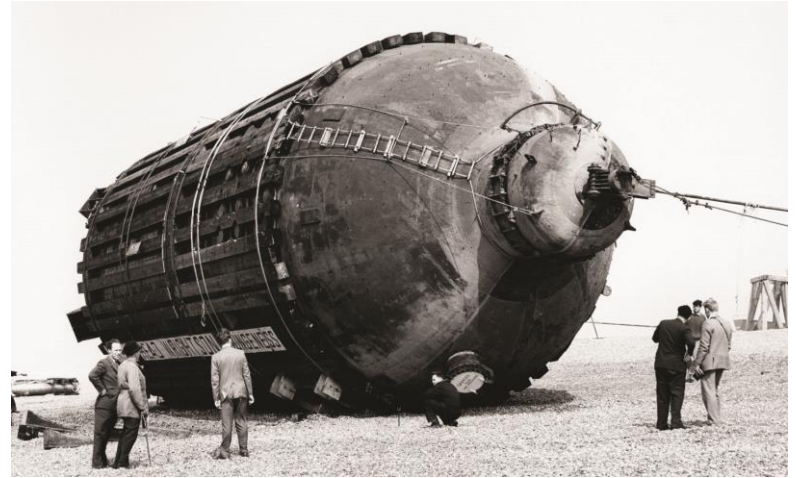

Asset Management

- Asset management projects are ongoing with £2.5 million in the budget for this year
- Projects will carry on as normal for the next financial year, there will be the same amount of people working on site



10 years of Magnox Socio-economic Funding Support 2012 - 2022

£9,165,583

Across all 12 Magnox sites in UK

Dungeness A

Funding awarded

£1,174,646

No. of applications supported

88

Additional NDA direct funding
2012-2022

£7,014,979

18 projects supported

Scotland 4 projects **£1,295,000**

Wales 8 projects **£4,370,000**

England 6 projects **£1,349,979**



Dungeness A applications 2022-23?

- **Total funding as of 10 November: £31,600:**
 - **Turn the Tide Festival** (Dymchurch) – Resources for Environmental Workshop £1,000
 - **Light Up New Romney** – Lantern-making materials £600
 - **Folkestone and Hythe District Council (on behalf of Romney Marsh Partnership Group)** - £30,000 towards the cost of employing a senior Specialist for the Romney Marsh Partnership.



Magnox Socio-economic Scheme

- Good Neighbour funding raised to £2,000; however, £6,000 allocation per site remains unchanged
- Kirsty Ramsden looks after Good Neighbour applications
- Applications over £2,000 by Haf Morris

- For further information please go to:
<https://www.gov.uk/government/collections/magnox-working-with-our-communities>
- Please feel free to contact Kirsty or Haf to discuss any potential applications (details on the above website)

10-year Magnox Anniversary Story

The full report, summary infographic and simplified guidance documents are available on:

<https://www.gov.uk/government/collections/magnox-working-with-our-communities>



Thank you

- Any questions?

